


INFORME DE AVANCE DE OBRA HASTA EL 31 DE MAYO

AVANCE POR FRENTE				
Frente	% parcial	Longitud	Peso	% total
AV. AMÉRICAS	87%	7330	0.36	32%
AV. MÉXICO	99%	320	0.02	2%
GRAN COLOMBIA	97%	3120	0.16	15%
AV. HUAYNA CÁPAC	82%	310	0.02	1%
MARISCAL LAMAR	96%	2520	0.13	12%
MARIANO CUEVA	18%	100	0.005	0%
GASPAR SANGURIMA	66%	470	0.02	2%
AV. ESPAÑA	67%	5920	0.29	20%
		20090	1.00	83.07%

AVANCE FÍSICO				
Área	Valor parcial	Peso	% parcial	% total
SISTEMAS	5%	0.05	22.3%	1.11%
ELECTRICIDAD	1%	0.01	48.2%	0.48%
VIARIO	23%	0.23	83.1%	19.11%
PATIO TALLER	22%	0.22	66.2%	14.57%
PUENTE YANUNCAY	4%	0.04	100.0%	4.00%
PUENTE TOMBAMBAMBA	3%	0.03	100.0%	3.00%
PUENTE MILCHICHIG	1%	0.01	14.6%	0.15%
MURO DE MILCHICHIG	5%	0.05	100.0%	5.00%
TRENES	16%	0.16	97.4%	15.58%
PARADAS	7%	0.07	30.5%	2.14%
SUBESTACIONES	13%	0.13	97.1%	12.62%
	100%	1		77.75%

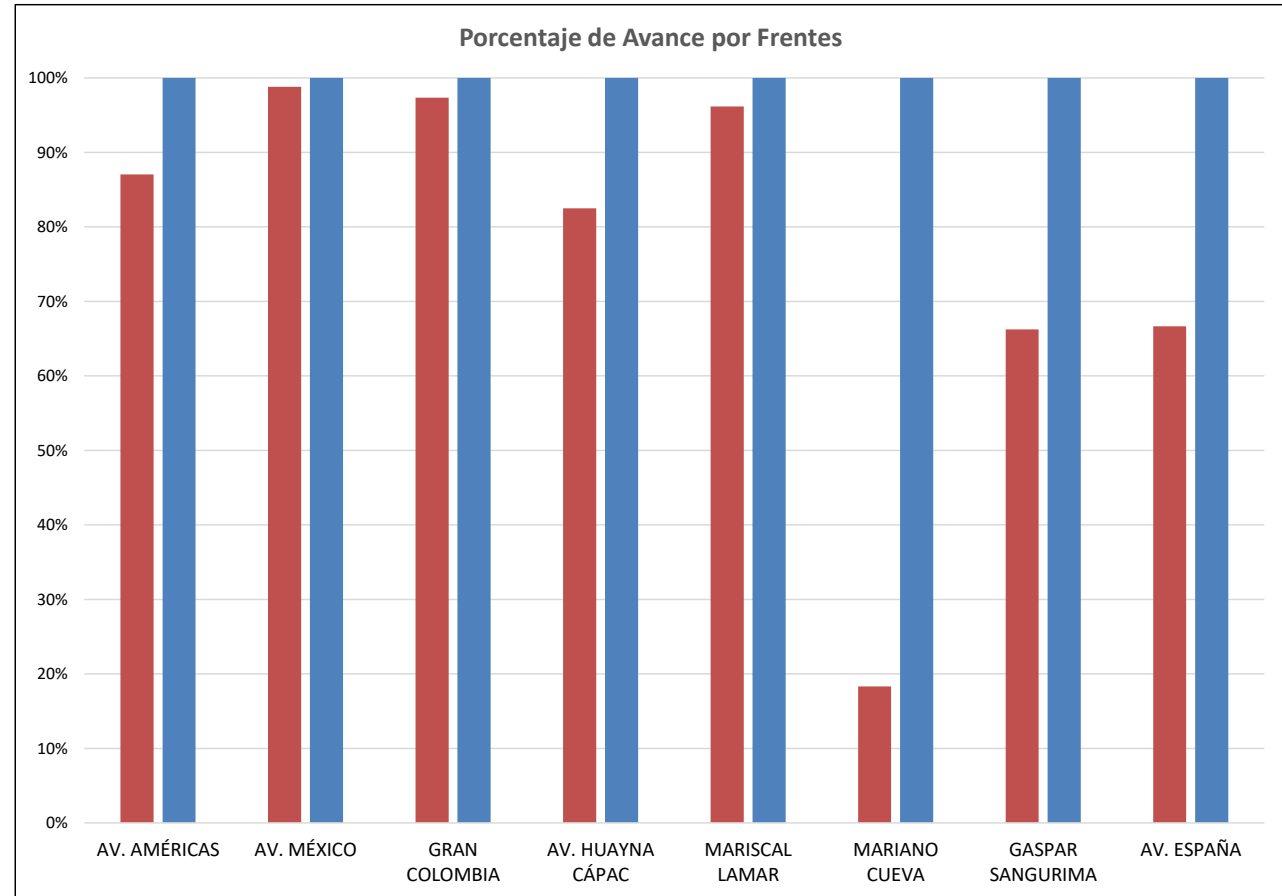

AVANCE ECONÓMICO	
CONTRATO CITA	\$ 142,600,000.00
CONTRATO CCRC	\$ 72,138,460.09
CONTRATOS CITA Y CCRC	\$ 219,400,356.43

PORCENTAJE TOTAL CITA Y CCRC	81.88%
------------------------------	---------------
